# Community Meeting

February 12, 2020



## Agenda

#### Projects in Design:

- Sub-Surface Frontiers Research Building (18<sup>th</sup> & Cheyanne) Design & Schedule Update
- South Campus Utilities Project (Schedule)
- Innovation Hub (13<sup>th</sup> and Maple Street) Design & Schedule Update
- Washington/18<sup>th</sup> Parking Garage & Beck Venture Center Design & Schedule Update
- Early Childhood Development Center (Mines Park 19<sup>th</sup> & Tangent Way) **Project currently on hold**

#### Mines current construction projects update:

- Parking Garage/Classroom Building (14<sup>th</sup> and Maple Street)
- 14<sup>th</sup> Street Construction Schedule
- Spruce Hall (19<sup>th</sup> and Illinois Street)
- Ops Buildings
- Wellness Center Addition
- Utility Infrastructure project/schedules

#### Questions/discussion

#### **Upcoming Events:**

- Spring Break March 21-29
- E-Day April 17-19
- Spring Commencement May 7<sup>th</sup> and 8<sup>th</sup>
- Summer Semester begins May 11<sup>th</sup>



# 18<sup>th</sup> Street Corridor




## 18<sup>th</sup> Street Corridor - 2022

#### Construction anticipated to begin Early 2020 and complete Summer/Fall 2022




## Subsurface Frontiers site

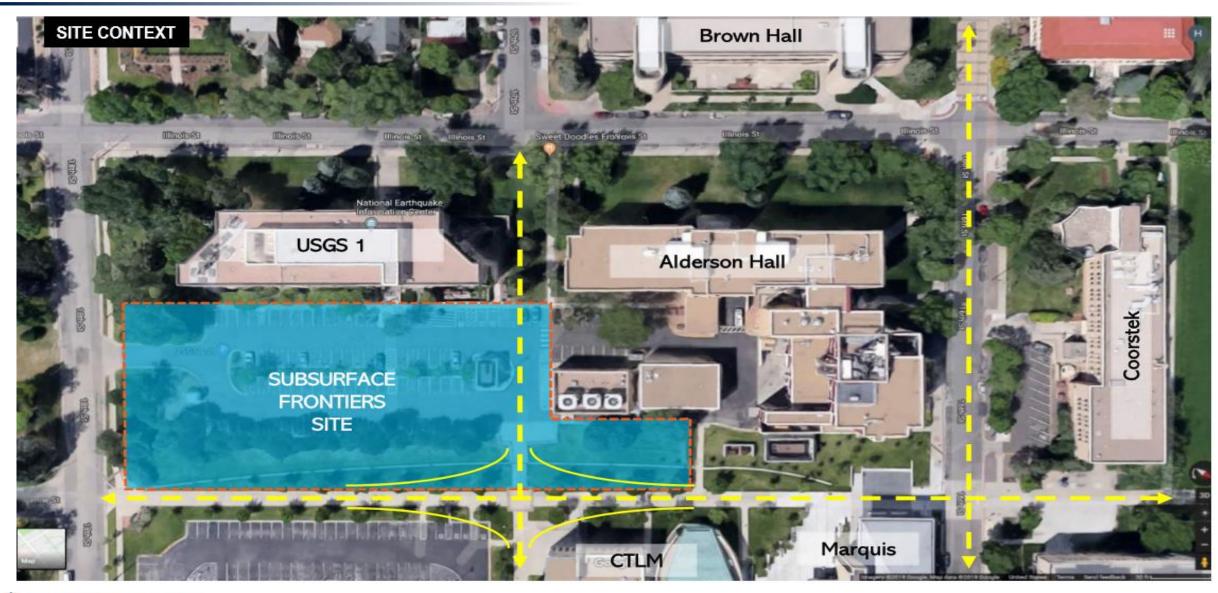



# SubSurface Frontiers Building - Brings 155 new jobs into Golden

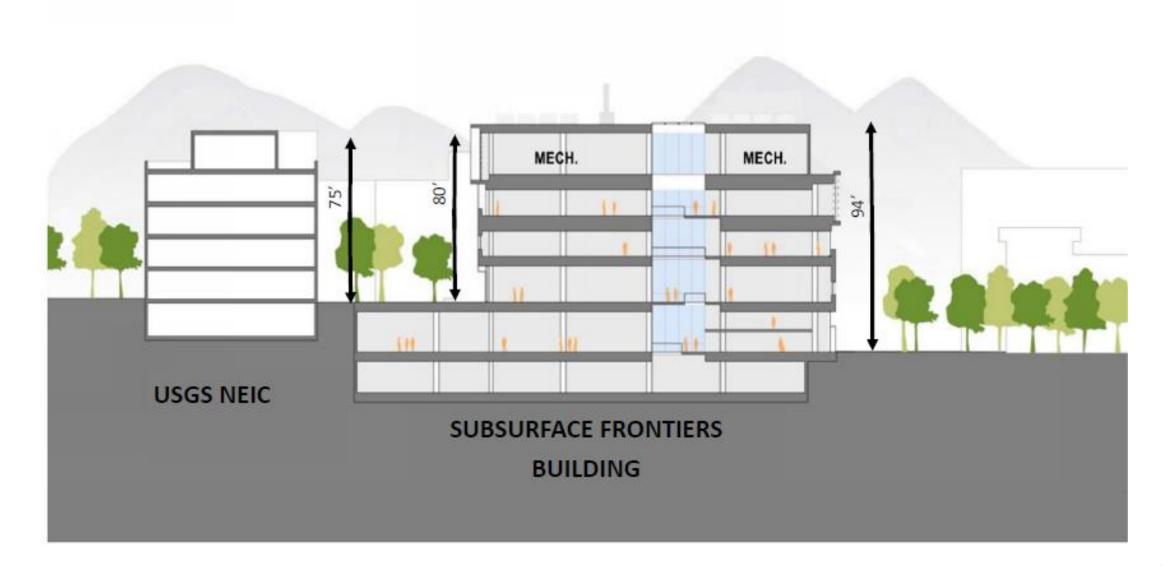

# Exterior – South View



## Exterior – East View





# East – Close View






# Exterior - North





# West Elevation - Courtyard

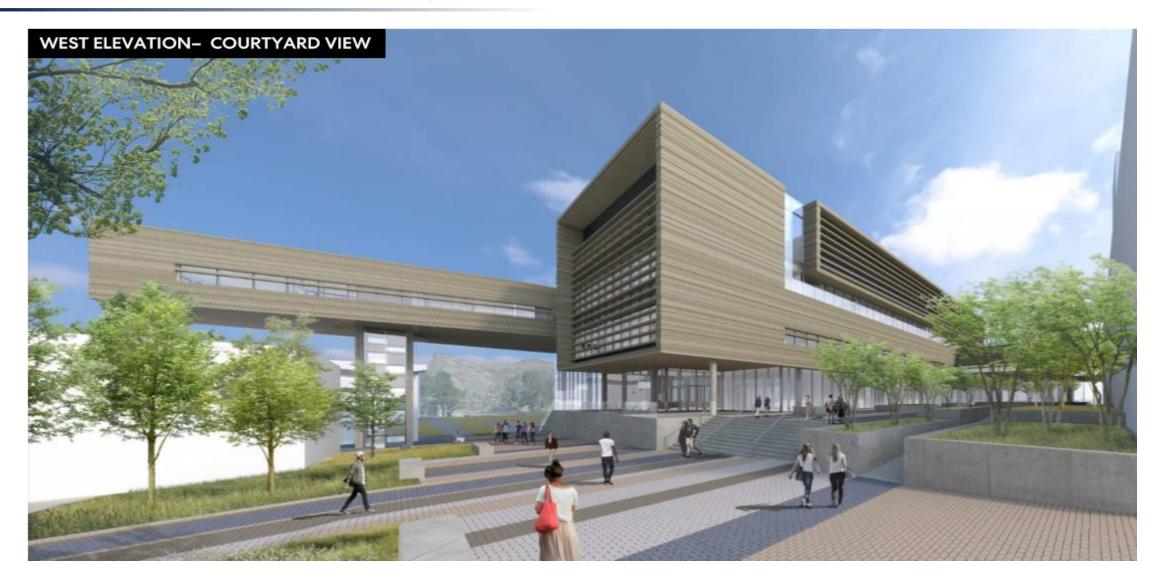






## Innovation Hub Site

#### **SITE PLANNING**

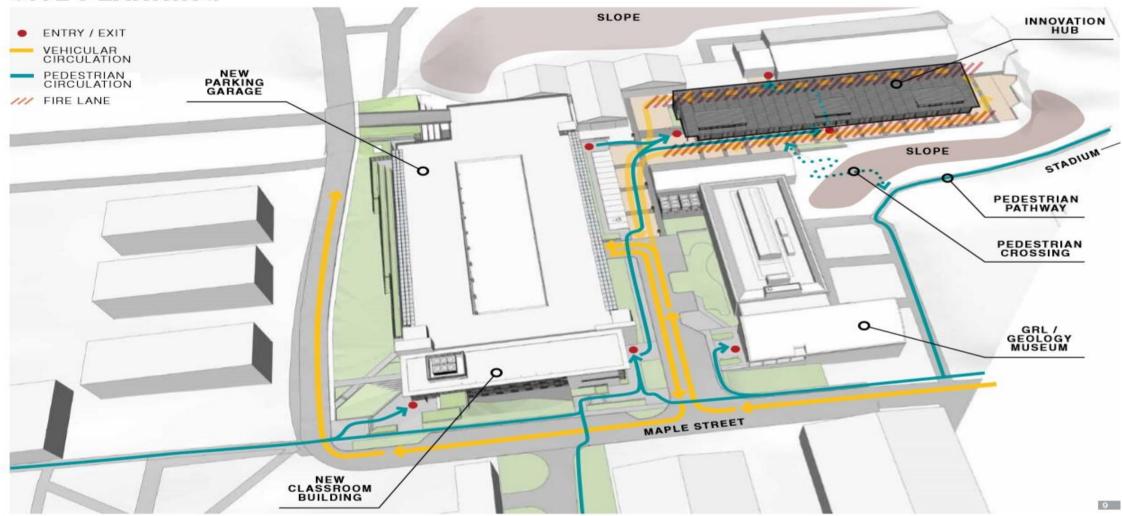



#### **BUILDING DESIGN**





#### **BUILDING DESIGN**





#### **BUILDING DESIGN**



#### **DESIGN**







**EXTERIOR DESIGN** 



#### **EXTERIOR DESIGN**






SITE PLANNING SETBACKS

CONCEPT DESIGN

NORTH SETBACK 5'
EAST SETBACK 15'
SOUTH SETBACK 34'
HEIGHT INCUBATOR 47'
HEIGHT GARAGE 61'

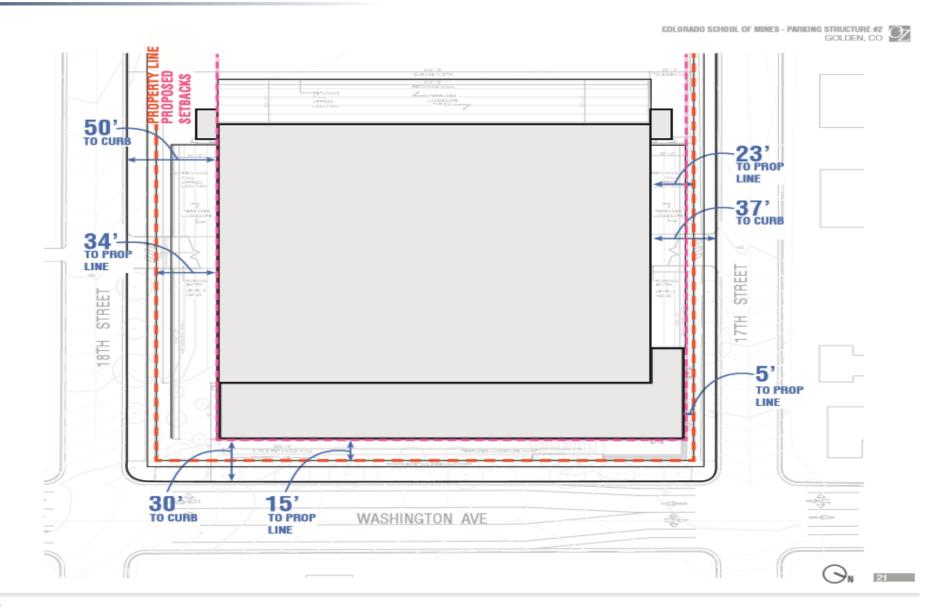







# Current Project Update



# Parking Garage 1

- 760 spaces
- 23,000 sf of classroom/office space
- Final concrete pours for garage early Feb
- Classroom is topped out, framing 25% complete
- Tracking summer 2020 completion








## 14<sup>th</sup> Street Extension

- Convert parking lot between Volk and Lakes to a through street
- Improvements for new pedestrian flow from Garage 1
- Work takes place spring and summer 2020

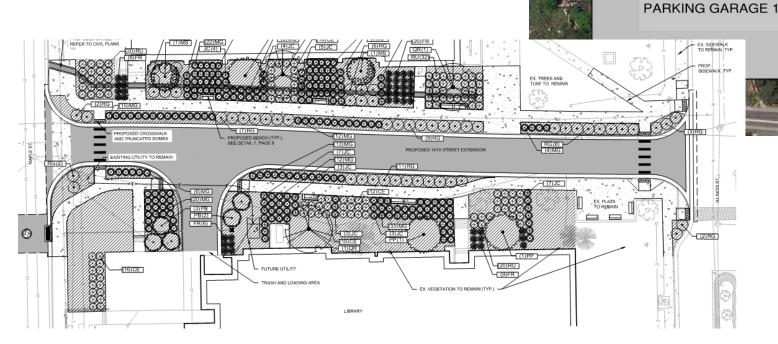



99 U 9 44 44 98 . 20944 H.

**VOLK GYM** 

# Spruce Hall

- 420 bed Freshmen housing
- Building is weather tight, starting drywall
- On target and on budget for Summer 2020 completion







# Ops Building and Moly Addition

- 12,000 square foot shop building complete and occupied
- 4500 sf office addition to Moly complete and occupied
- New gravel lot with 120 parking spaces in Mines Park complete







## Wellness Center Addition

- 1200 Square foot addition to the second floor
- Offices and support space for student counseling
- Tracking a May 2020 completion





# Campus Utility Infrastructure Improvements

- New steam and chilled water infrastructure
- Steam and Chilled Water on 18<sup>th</sup> streets (west of Illinois St.) is 40% complete finishes Dec 2019
- Second phase of work (within existing tunnel) on Maple at 16<sup>th</sup> Street spring 2020
- Future tunnel work crossing Illinois St. within 18<sup>th</sup> St. to Cheyenne St. (Closures possible Summer 2020)





# Questions

